


Programme 1 - East Lancashire Strategic Cycleway Network Delivery Programme (13/10/15)

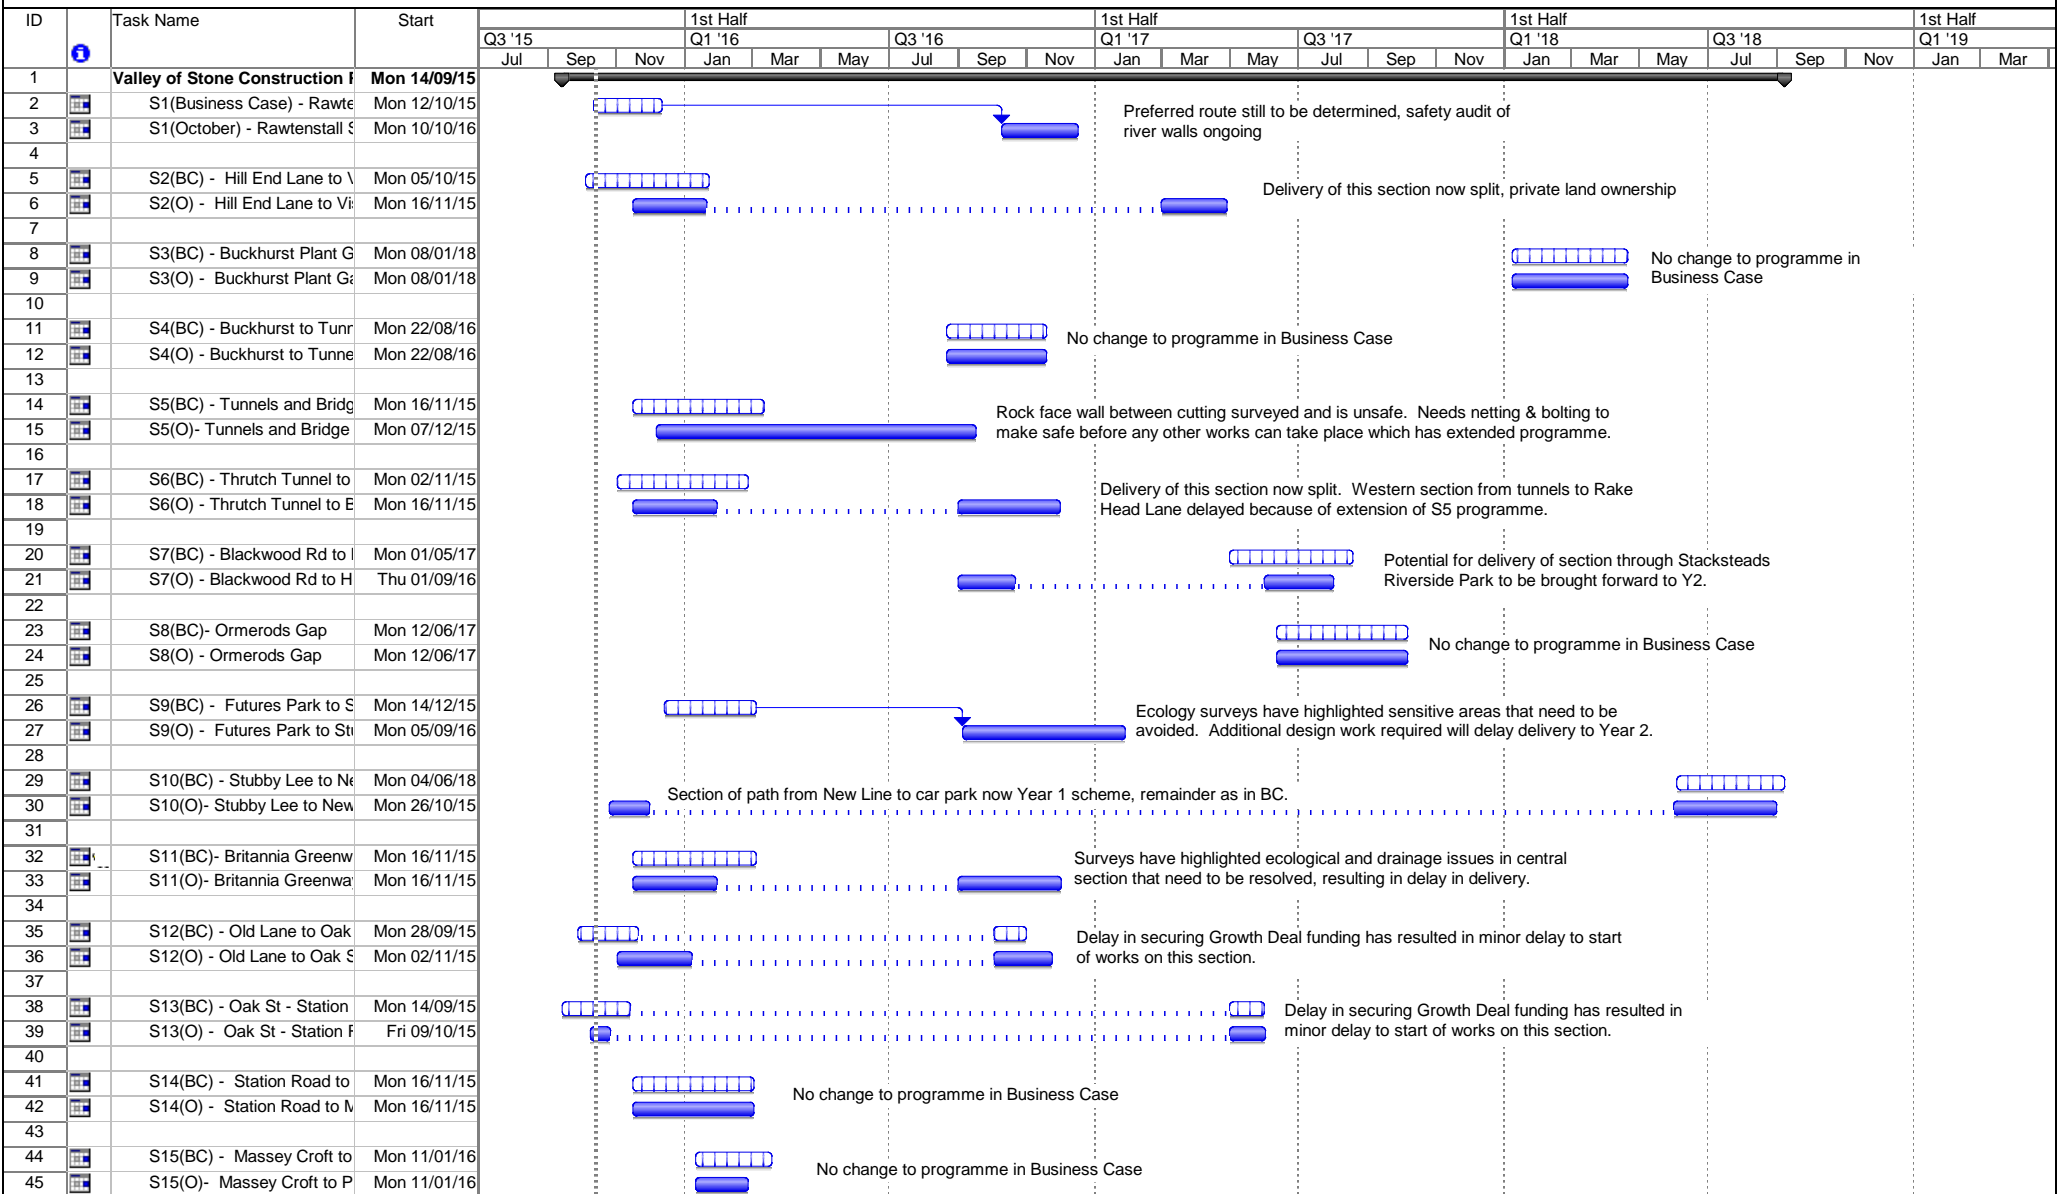

Project: East Lancs Cycleway Network
Date: Tue 13/10/15

Task: [Blue bar] Progress
Split: [Dotted line] Milestone

Summary: [Grey bar] External Tasks
Project Summary: [Grey bar with arrow] External Milestone

Deadline: [Green arrow]

Programme 1 - East Lancashire Strategic Cycleway Network Delivery Programme (13/10/15)


ID	Task Name	Start	1st Half									1st Half									1st Half			1st Half		
			Q3 '15			Q1 '16			Q3 '16			Q1 '17			Q3 '17			Q1 '18			Q3 '18			Q1 '19		
			Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	
46																										
47																										
48	National Cycle Route 6 Constr	Fri 04/09/15																								
49	S1(BC) - Woodnook Green	Mon 05/10/15	<p>Clearance & minor improvements of site to take place Q3, potential resurfacing in Year 4.</p>																							
50	S1(O) - Woodnook Greenw	Mon 02/11/15																								
51																										
52	S2(BC) - Baxenden - Rising	Mon 20/08/18																								
53	S2(O) - Baxenden - Rising	Mon 20/08/18	<p>No change to programme in Business Case currently proposed. Could be delivered earlier if negotiations with private landowners are positive</p>																							
54																										
55	S3(BC) - Rising Bridge Road	Mon 16/11/15																								
56	S3(O) - Rising Bridge Road	Mon 10/10/16	<p>Scope and timing of work on this section dependent on preferred route for S2. Discussions needed with private landowners.</p>																							
57																										
58	S4(BC) - Hud Hey Road	Mon 25/01/16																								
59	S4(O) - Hud Hey Road	Mon 12/09/16	<p>Design of this section including location of potential crossing dependent on progress with Sections 2 & 3.</p>																							
60																										
61	S5(BC) - Hud Hey Road - B	Mon 14/05/18																								
62	S5(O) - Hud Hey Rd - Bootl	Mon 13/03/17	<p>Preferred route option for Sections 5 - 8 still to be determined (could be either side of A56), sections need to be delivered at a similar time.</p>																							
63																										
64	S6(BC) - Booth St - Comm	Mon 13/08/18																								
65	S6 (O) - Booth St - Comm	Mon 19/09/16	<p>See Section 5.</p>																							
66																										
67	S7(BC) - Well Bank	Mon 14/05/18																								
68	S7(O) - Well Bank	Mon 06/03/17	<p>See Section 5</p>																							
69																										
70	S8(BC) - Flip Road - Grane	Mon 04/07/16																								
71	S8(O) - Flip Road - Grane F	Mon 03/10/16	<p>See Section 5</p>																							
72																										
73	S9(BC) - Swinnel & Ogden	Mon 21/09/15																								
74	S9(O) - Swinnel & Ogden B	Mon 30/11/15	<p>Delivery of this section now split. Ecology issues including newts to resolve to south of Ogden Brook, Construction access required from south across Viaduct.</p>																							
75																										
76	S10(BC) - Helmshore Viad	Mon 12/09/16																								
77	S10(O) - Helmshore Viaduc	Mon 12/09/16	<p>No change to programme in Business Case currently proposed. Potential ecology (bats and newts) issues to resolve.</p>																							
78																										
79	S11(BC) - Bridge End Clos	Mon 19/10/15																								
80	S11(O) - Bridge End Close	Mon 23/11/15	<p>Delay in securing Growth Deal funding has resulted in minor delay to start of works on this section.</p>																							
81																										
82	S12(BC) - Station Road	Mon 07/12/15																								
83	S12(O) - Station Road	Mon 09/05/16	<p>Additional design work required on crossing of Helmshore Road has delayed delivery of this section.</p>																							
84																										
85	S13(BC) - Snigg Hole	Mon 15/08/16																								
86	S13(O) - Snigg Hole	Mon 14/03/16	<p>Alternative route through park identified which could potentially be delivered in Year 1. Requires agreement from Rossendale BC.</p>																							
87																										
88	S14(BC) - Irongate Lane	Mon 15/02/16																								
89	S14(O) - Irongate Lane	Mon 10/04/17	<p>Drainage issues identified, requires additional design work. Agreement with private landowners required.</p>																							
90																										

Project: East Lancs Cycleway Network Date: Tue 13/10/15

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

Programme 1 - East Lancashire Strategic Cycleway Network Delivery Programme (13/10/15)

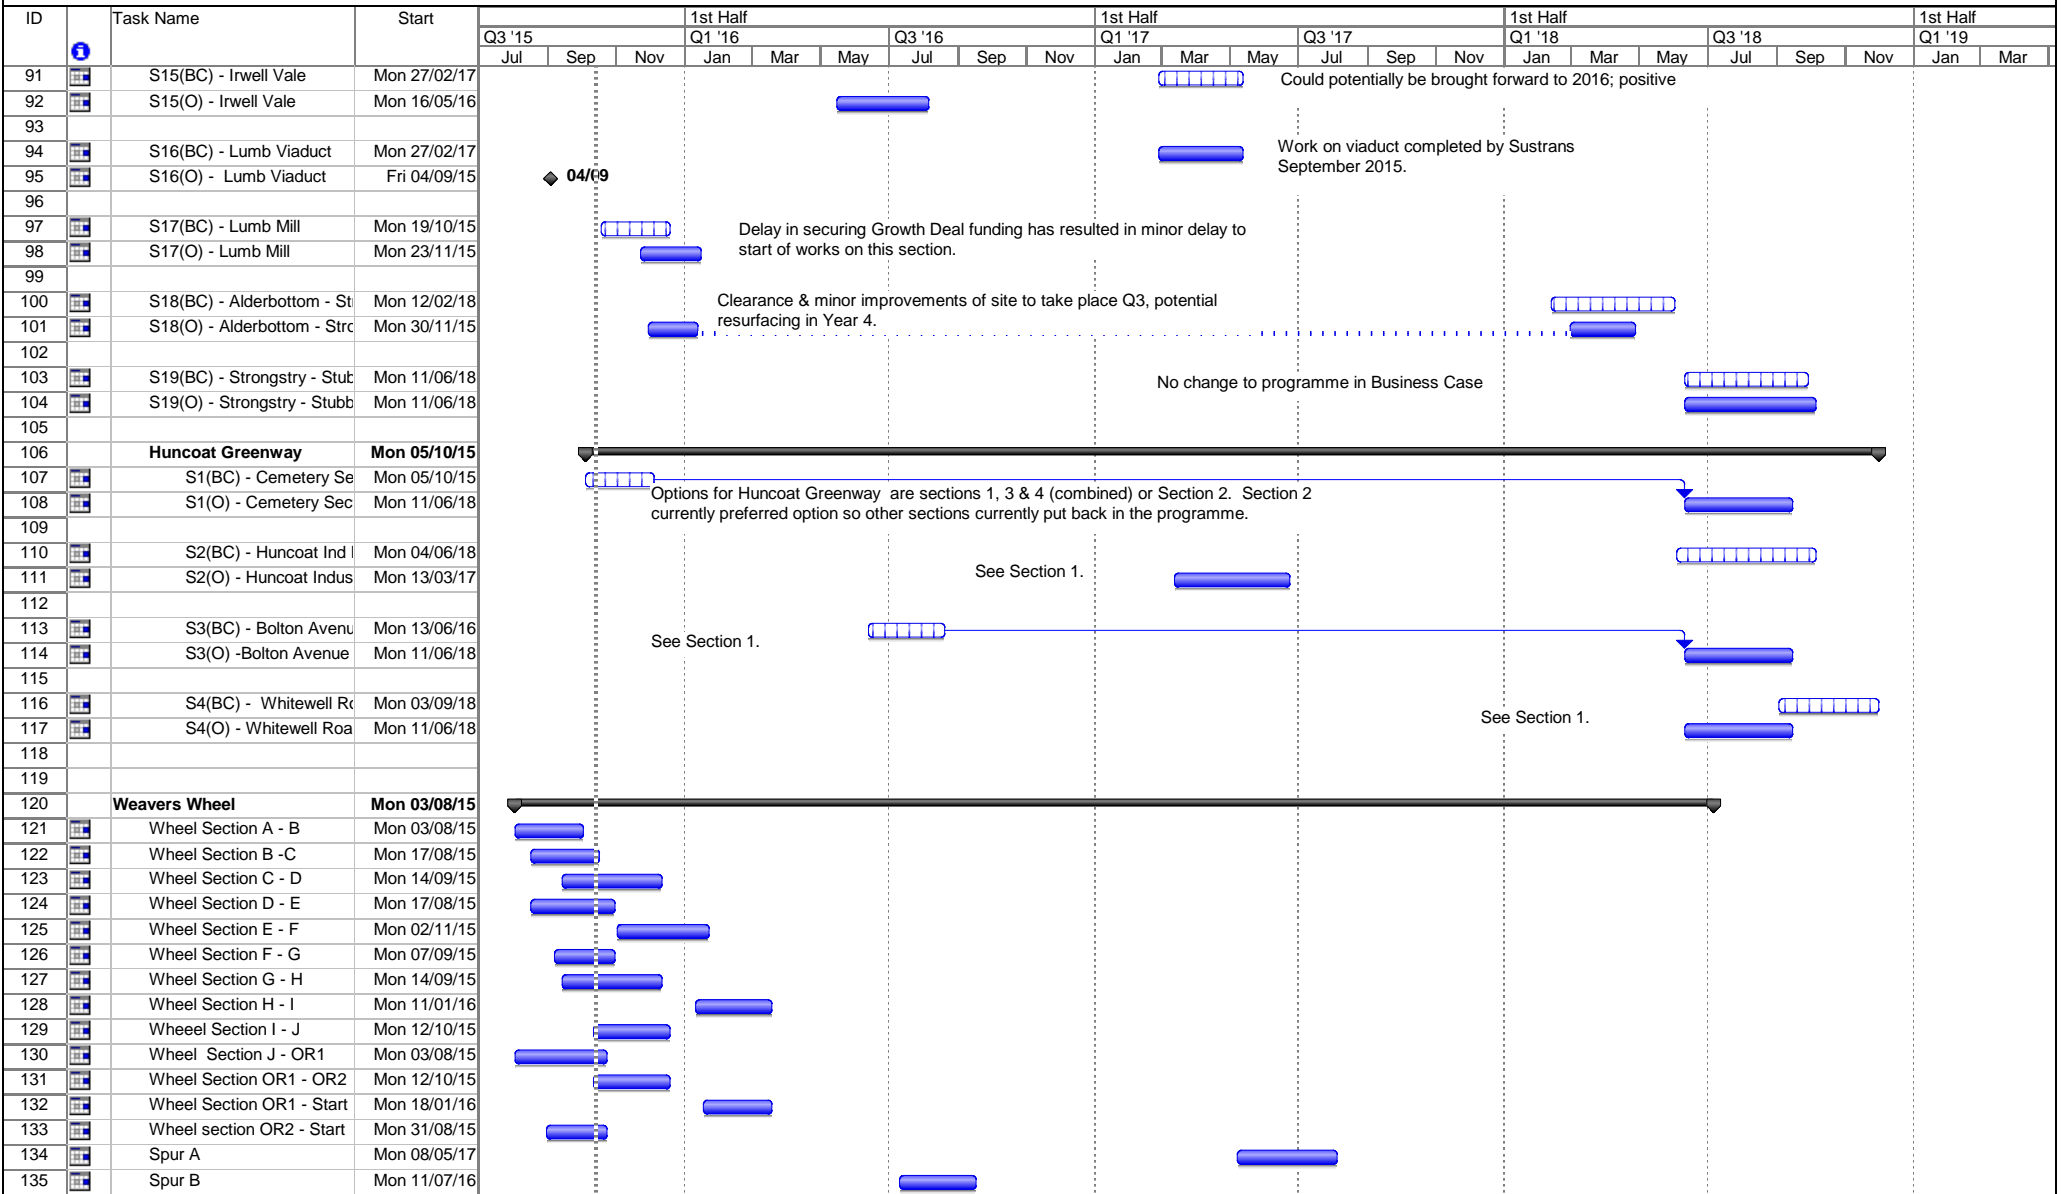

Project: East Lancs Cycleway Network
Date: Tue 13/10/15

Task: [Blue bar] Progress
Split: [Dotted bar] Milestone

Summary: [Thick black bar] Project Summary
External Tasks: [Thin black bar with arrow] External Milestone

Deadline: [Grey bar with arrow] [Green down arrow]

Programme 1 - East Lancashire Strategic Cycleway Network Delivery Programme (13/10/15)

ID	Task Name	Start	1st Half									1st Half									1st Half								
			Q3 '15			Q1 '16			Q3 '16			Q1 '17			Q3 '17			Q1 '18			Q3 '18			Q1 '19					
			Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar				
136	Spur C	Mon 12/06/17																											
137	Spur D	Mon 07/09/15		█																									
138	Spur E	Mon 09/04/18																											
139	Spur F	Mon 09/05/16																											
140	Spur G	Mon 07/05/18																											
141	Spur H	Mon 11/09/17																											
142	Spur I	Mon 23/05/16																											
143	Spur J	Mon 15/02/16																											
144	Spoke 1	Mon 23/11/15																											
145	Spoke 2	Mon 19/10/15																											
146	Spoke 3	Mon 08/05/17																											
147	Spoke 4	Mon 10/08/15																											
148	Spoke 5	Mon 14/09/15																											
149	Spoke 6	Mon 05/10/15																											

Project: East Lancs Cycleway Network
Date: Tue 13/10/15

Task: Progress Summary External Tasks Deadline

Split: Milestone Project Summary External Milestone Milestone
